

-	*	Building Exterior	160d	Mon 8/21	Fri 3/30/1
	*	Installation of aluminum railing at Third Floor Deck	10d	Mon 2/5/	Fri 2/16/1
	*	Application of cementitious waterproofing to Third Floor Deck	12d	-	Fri 2/2/18
	*	Concrete repairs to Third Floor Deck	15d	Thu 12/2	Wed 1/17
	*	Removal of deck finish	4d		Wed 12/2
	*	Third Floor Deck railing wall demolition Set up of temporary railing	4d 2d		Tue 12/19 Thu 12/21
	k			12/11/17	12/13/17
	*	Set up of scaffolding/overhead protection on East side of property	3d		Wed
	*	Third Floor Deck	20 50d		Fri 2/16/1
	*	Clean up of Pool deck	12a 2d		Fri 10/13/
	*	Replace existing deck drains Apply cementitious waterproofing to Pool deck	3d 12d		Wed 9/27, Fri 10/13/
		Concrete repairs to Pool deck	20d		Fri 9/22/1
		Pool deck finish removal	3d	-	Fri 8/25/1
	*	Install waterline tile, depth markers, swimming lane	5d	-	Wed 10/2
		Apply Pebble Tec Pool finish	5d	-	Wed 10/1
	*	Install Pool coping, lights, ladders, and rails	7d		Wed 10/1
	*	Apply Sto Watertight Coat to Pool Surface	5d		Mon 10/2,
	*	Concrete repairs to Pool surface	20d	Tue 8/29/	Mon 9/25
	*	Engineer to mark areas of repair for Pool surface	1d	Mon 8/28	Mon 8/28
	*	Removal of existing finishes, ladders, rails, lights, coping and gutters at pool	5d	Mon 8/21/17	Fri 8/25/17
	*	Pool and Pool Deck	50d	Mon 8/21	Fri 10/27/
	*	Cleaning up of area on North Side of garage	1d	Fri 10/20,	Fri 10/20/
	*	Chipping concrete, application of Sika Armatect CI, inspection by engineer and pouring back concrete	30d		Thu 10/19/17
	*	Engineer to mark areas of repair for North side of garage	1d		Thu 9/7/1
	*	Setting up of shoring per shoring plan and protection	1d		Thu 9/7/1
	*	Garage South Side	32d	Thu 9/7/1	Fri 10/20/
	*	Cleaning up of area on North Side of garage	1d	Wed 9/6/	Wed 9/6/1
	*	Chipping concrete, application of Sika Armatect CI, inspection by engineer and pouring back concrete	31d	Tue 7/25/17	Tue 9/5/17
	•	Engineer to mark areas of repair for North side of garage	1d	Mon 7/24	Mon 7/24,
	*	Setting up of shoring per shoring plan and protection	1d	Mon 7/24	Mon 7/24,
	*	Garage North Side	33d	Mon 7/24	Wed 9/6/:
1	*	Construction of job container in garage/setting up of work area	2d	Thu 7/20,	Fri 7/21/1

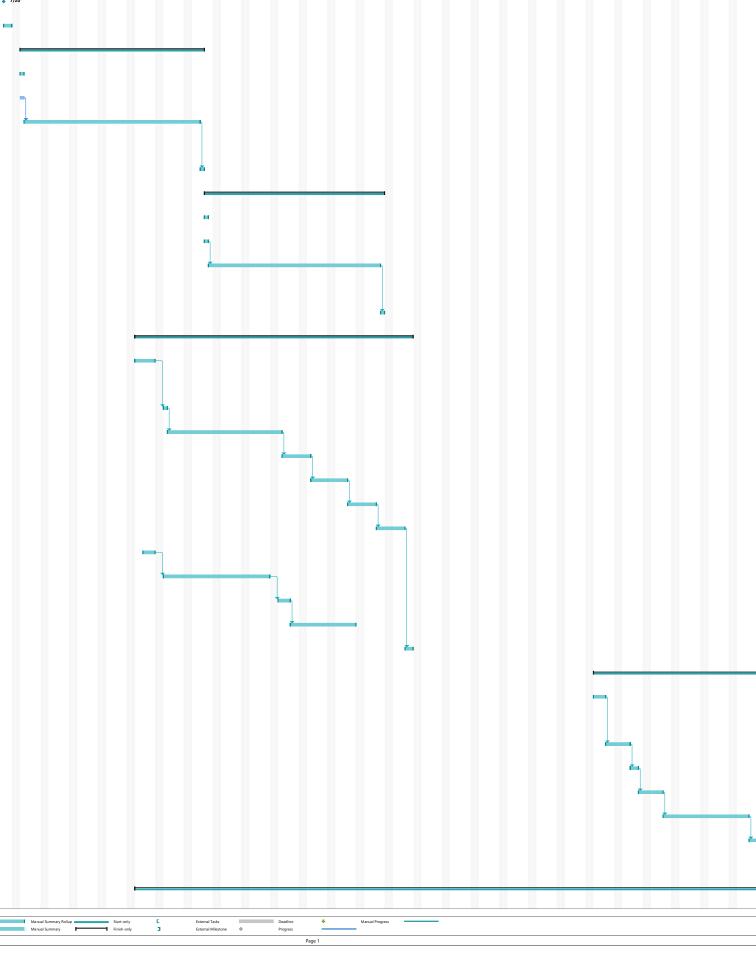


	Mode	Line 1	40d	Mon 8/21	Finish Fri 10/13/:
	*	Set up protection/rigging	2d	Mon 8/21	Tue 8/22/
	*	Engineer to mark concrete repairs	1d	Wed 8/23	Wed 8/23/
	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu 8/24/17	Wed 10/4/17
	*	Paint exterior of building	5d	Thu 10/5,	Wed 10/1:
	*	Clean up/move swingstage	2d	Thu 10/12	Fri 10/13/
	*	Line 2	40d	Mon 8/21	Fri 10/13/
	*	Set up protection/rigging	2d	Mon 8/21	Tue 8/22/1
	*	Engineer to mark concrete repairs	1d	Wed 8/23	Wed 8/23/
	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu 8/24/17	Wed 10/4/17
	*	Paint exterior of building	5d	Thu 10/5,	Wed 10/11
	*	Clean up/move swingstage	2d	Thu 10/12	Fri 10/13/:
	*	Line 3	40d	Mon 8/21	Fri 10/13/:
	*	Set up protection/rigging	2d	Mon 8/21	Tue 8/22/1
	*	Engineer to mark concrete repairs	1d	Wed 8/23	Wed 8/23/
	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu 8/24/17	Wed 10/4/17
	*	Paint exterior of building	5d	Thu 10/5,	Wed 10/11
	*	Clean up/move swingstage	2d	Thu 10/12	Fri 10/13/
	*	Line 4	40d	Mon 8/21	Fri 10/13/:
	*	Set up protection/rigging	2d	Mon 8/21	Tue 8/22/1
	*	Engineer to mark concrete repairs	1d	Wed 8/23	Wed 8/23/
	*	Removal of Aluminum Railing	2d	Thu 8/24,	Fri 8/25/17
	*	Concrete repairs per Engineer's specifications	20d	Mon 8/28	Fri 9/22/17
	*	Installation of Aluminum Railing	8d	Mon 9/25	Wed 10/4/
	*	Paint exterior of building	5d	Thu 10/5,	Wed 10/11
	*	Clean up/move swingstage	2d	Thu 10/12	Fri 10/13/:
	*	Line 5	40d	Mon 8/21	Fri 10/13/:
	*	Set up protection/rigging	2d	Mon 8/21	Tue 8/22/1
	*	Engineer to mark concrete repairs	1d	Wed 8/23	Wed 8/23/
	*	Removal of Aluminum Railing	2d	Thu 8/24,	Fri 8/25/17
	*	Concrete repairs per Engineer's specifications	20d	Mon 8/28	Fri 9/22/17
	*	Installation of Aluminum Railing	8d	Mon 9/25	Wed 10/4/
	*	Paint exterior of building	5d	Thu 10/5,	Wed 10/11
	*	Clean up/move swingstage	2d	Thu 10/12	Fri 10/13/:
1	*	Line 6	40d	Mon 8/21	Fri 10/13/

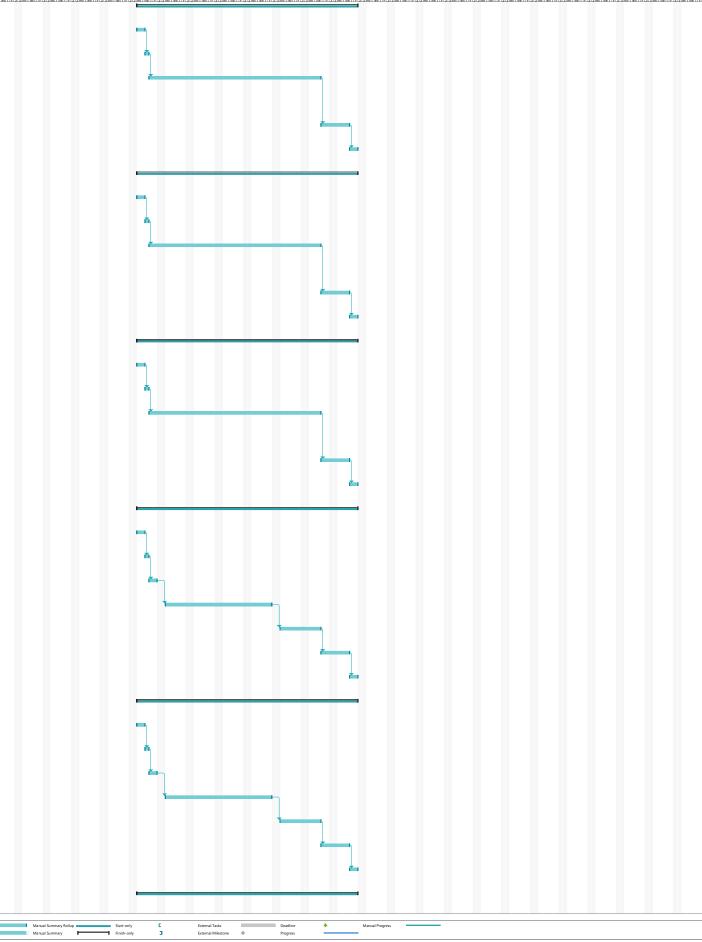

Page 2


17 Jul 2, 18 Jul 2, 17 Jul 2, 18 Jul 2, 19 Jul 2, 17 Jul 2, 18 Jul 2, 17 Jul 2, 18 Jul

Task Task Name	Duration	Start Finish
Set up protection/rigging	2d	Mon 8/21Tue 8/22/2
* Engineer to mark concrete repairs	1d	Wed 8/23Wed 8/23,
* Removal of Aluminum Railing	2d	Thu 8/24/Fri 8/25/1
Concrete repairs per Engineer's specifications	20d	Mon 8/28Fri 9/22/1
* Installation of Aluminum Railing	8d	Mon 9/25Wed 10/4,
 Paint exterior of building 	5d	Thu 10/5/Wed 10/1:
* Clean up/move swingstage	2d	Thu 10/17Fri 10/13/
* Line 7	40d	Mon 10/1Fri 12/8/1
* Set up protection/rigging	2d	Mon 10/1Tue 10/17
Engineer to mark concrete repairs	1d	Wed 10/1Wed 10/18
Removal of Aluminum Railing	2d	Thu 10/19Fri 10/20/
Concrete repairs per Engineer's specifications	20d	Mon 10/2Fri 11/17/
Installation of Aluminum Railing	8d	Mon 11/2Wed 11/29
Paint exterior of building	5d	Thu 11/3(Wed 12/6)
* Clean up/move swingstage	2d	Thu 12/7/Fri 12/8/1
* Line 8	40d	Mon 10/1Fri 12/8/1
* Set up protection/rigging	2d	Mon 10/1Tue 10/17
* Engineer to mark concrete repairs	1d	Wed 10/1Wed 10/18
* Removal of Aluminum Railing	2d	Thu 10/1!Fri 10/20/
* Concrete repairs per Engineer's specifications	20d	Mon 10/2Fri 11/17/2
* Installation of Aluminum Railing	8d	Mon 11/2Wed 11/29
* Paint exterior of building	5d	Thu 11/3(Wed 12/6,
* Clean up/move swingstage	2d	Thu 12/7/Fri 12/8/1
* Line 9	40d	Mon 10/1Fri 12/8/1
* Set up protection/rigging	2d	Mon 10/1Tue 10/17
* Engineer to mark concrete repairs	1d	Wed 10/1Wed 10/18
* Removal of Aluminum Railing	2d	Thu 10/1!Fri 10/20/
Concrete repairs per Engineer's specifications	20d	Mon 10/2Fri 11/17/2
* Installation of Aluminum Railing	8d	Mon 11/2Wed 11/29
* Paint exterior of building	5d	Thu 11/3(Wed 12/6)
* Clean up/move swingstage	2d	Thu 12/7/Fri 12/8/1
* Line 10	40d	Mon 10/1Fri 12/8/1
* Set up protection/rigging	2d	Mon 10/1Tue 10/17
* Engineer to mark concrete repairs	1d	Wed 10/1Wed 10/18
* Removal of Aluminum Railing	2d	Thu 10/19Fri 10/20/2
Concrete repairs per Engineer's specifications	20 20d	Mon 10/2Fri 11/17/2
-		Mon 11/2Wed 11/29
* Paint exterior of building	5d	Thu 11/3(Wed 12/6,
* Ins	tallation of Aluminum Railing	tallation of Aluminum Railing 8d nt exterior of building 5d

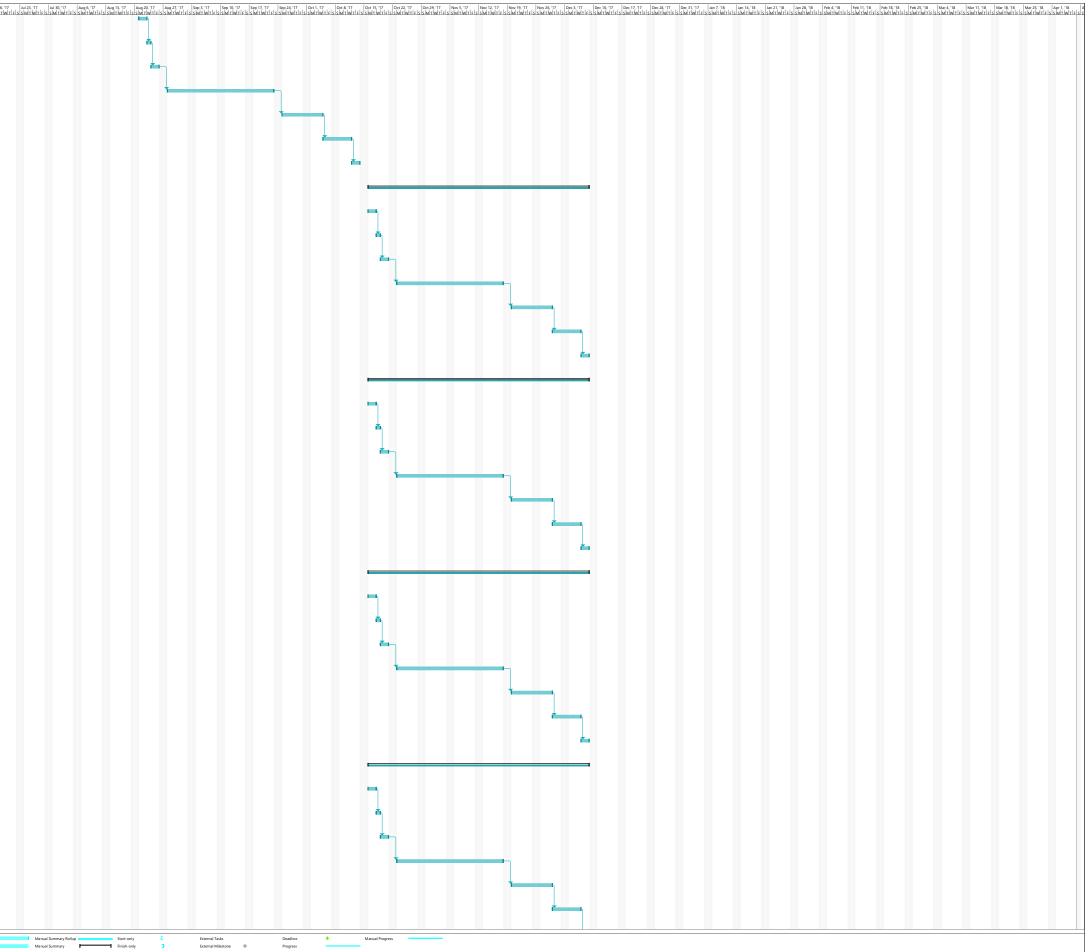

Page 3


08	Mode	Clean up/move swingstage	2d	Thu 12/7,Fri 12/8/1
19	*	Line 11	40d	Mon 10/1Fri 12/8/1
10	*	Set up protection/rigging	2d	Mon 10/1Tue 10/17
1	*	Engineer to mark concrete repairs	1d	Wed 10/1Wed 10/1
2	*	Removal of Aluminum Railing	2d	Thu 10/1(Fri 10/20/
3	*	_	20d	Mon 10/2Fri 11/17/
4		Concrete repairs per Engineer's specifications		
	ĺ.	Installation of Aluminum Railing	8d	Mon 11/2Wed 11/2
15	*	Paint exterior of building	5d	Thu 11/3(Wed 12/6
16	*	Clean up/move swingstage	2d	Thu 12/7/Fri 12/8/1
17	*	Line 12	40d	Mon 10/1Fri 12/8/1
18	*	Set up protection/rigging	2d	Mon 10/1Tue 10/17
19	*	Engineer to mark concrete repairs	1d	Wed 10/1Wed 10/1
20	*	Removal of Aluminum Railing	2d	Thu 10/1!Fri 10/20/
21	*	Concrete repairs per Engineer's specifications	20d	Mon 10/2Fri 11/17/
22	*	Installation of Aluminum Railing	8d	Mon 11/2Wed 11/2
23	*	Paint exterior of building	5d	Thu 11/3(Wed 12/6
24	*	Clean up/move swingstage	2d	Thu 12/7/Fri 12/8/1
25	*	Line 13	40d	Mon 12/1Fri 2/2/18
26	*	Set up protection/rigging	2d	Mon 12/1Tue 12/12
27	*	Engineer to mark concrete repairs	1d	Wed 12/1Wed 12/1
28	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu Wed 12/14/17 1/24/18
19	*	Paint exterior of building	5d	Thu 1/25,Wed 1/31
0	*	Clean up/move swingstage	2d	Thu 2/1/1Fri 2/2/18
81	*	Line 14	40d	Mon 12/1Fri 2/2/18
32	*	Set up protection/rigging	2d	Mon 12/1Tue 12/12
13	*	Engineer to mark concrete repairs	1d	Wed 12/1Wed 12/1
34	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu Wed 12/14/17 1/24/18
85	*	Paint exterior of building	5d	Thu 1/25,Wed 1/31
6	*	Clean up/move swingstage	2d	Thu 2/1/1Fri 2/2/18
87	*	Line 15	40d	Mon 12/1Fri 2/2/18
38	*	Set up protection/rigging	2d	Mon 12/1Tue 12/12
39	*	Engineer to mark concrete repairs	1d	Wed 12/1Wed 12/1
40	*	Removal of stucco finish, repair concrete per Engineer's	30d	Thu Wed
		specifications, reapply stucco	300	12/14/171/24/18
11	*	Paint exterior of building	5d	Thu 1/25,Wed 1/31
12	*	Clean up/move swingstage	2d	Thu 2/1/1Fri 2/2/18

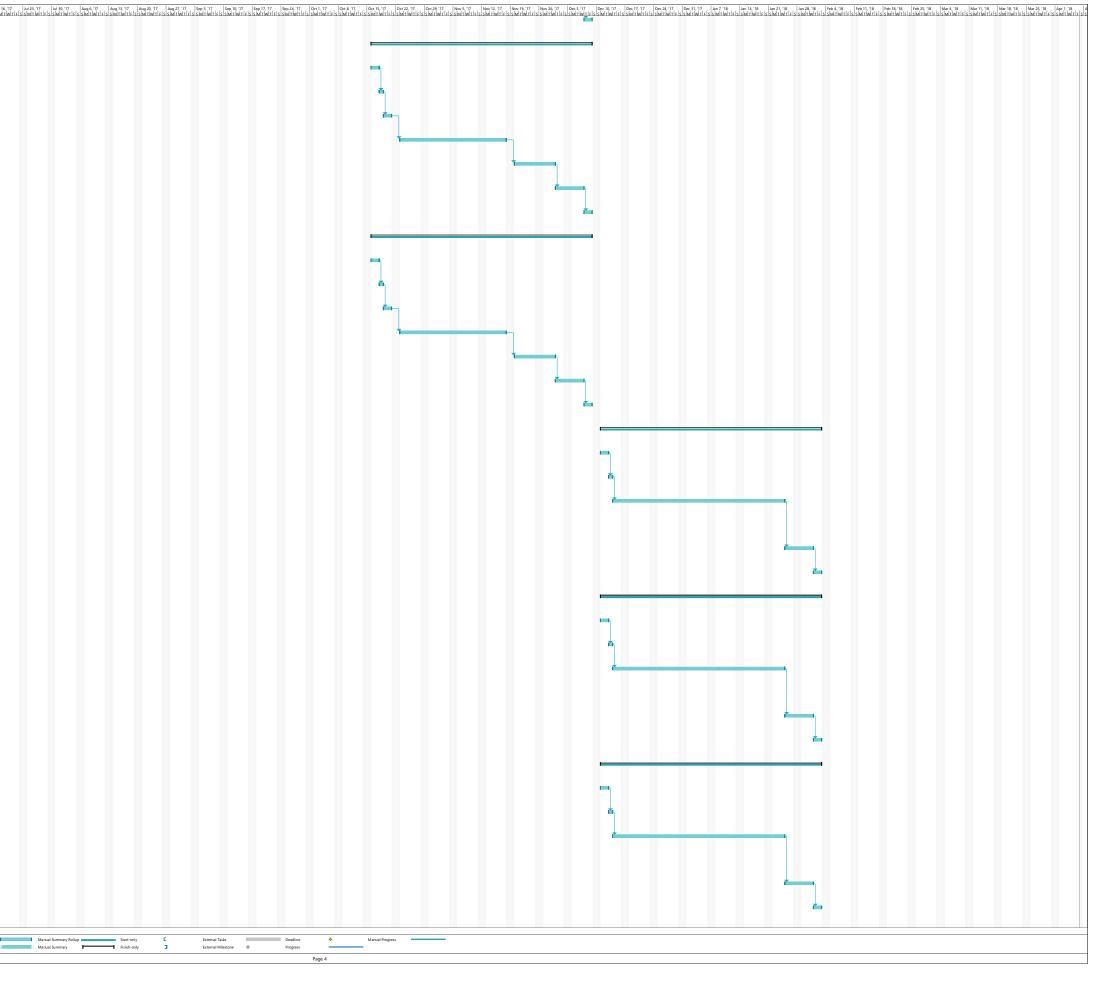

Marual Summary Rollup Start-only C Marual Summary Finish-only 3

Mode	Task Name le	Duration	Start Finish 16, 17 Jul 23 MTWTFESSMT	Jul 30, '17 Aug 6, '17 Aug 13, '17 Aug 20, '17 IEIS SMITHUTES SMITHUTES SMITHUTES SMITHUTE	Aug 27, '17 Sep 3, '17 Sep 10, '17 SSM TWTFESSMTWTFESSMTWTFES	MTWTIELS SMTWTIELS SMTWTIELS	SMTWTESSMTWTESS	MTWTFSSMTWT	SSMTWTFSSN	TWTESSMTWTE	SISIMITIWITIFISISIN	ITWITIFIS SMITW	tifisisi
1	Line 16	40d	Mon 12/1Fri 2/2/18										
*	Set up protection/rigging	2d	Mon 12/1Tue 12/12,									-	
*	Engineer to mark concrete repairs	1d	Wed 12/1Wed 12/13									ň	
	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu Wed 12/14/17 1/24/18									i	ł
*	Paint exterior of building	5d	Thu 1/25,Wed 1/31/										
*	Clean up/move swingstage	2d	Thu 2/1/1Fri 2/2/18										
*	Line 17	40d	Mon 12/1Fri 2/2/18									-	_
*	Set up protection/rigging	2d	Mon 12/1Tue 12/12,									-	
*	Engineer to mark concrete repairs	1d	Wed 12/1Wed 12/13									ň	
*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu Wed 12/14/17 1/24/18										
*	Paint exterior of building	5d	Thu 1/25,Wed 1/31/										
*	Clean up/move swingstage	2d	Thu 2/1/1Fri 2/2/18										
*	Line 18	40d	Mon 12/1Fri 2/2/18									-	+
*	Set up protection/rigging	2d	Mon 12/1Tue 12/12,									-	
*	Engineer to mark concrete repairs	1d	Wed 12/1Wed 12/13									ň	
*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu Wed 12/14/17 1/24/18									i	ł
*	Paint exterior of building	5d	Thu 1/25,Wed 1/31/										
*	Clean up/move swingstage	2d	Thu 2/1/1Fri 2/2/18										
*	Line 19	40d	Mon 2/5/Fri 3/30/18										
*	Set up protection/rigging	2d	Mon 2/5/Tue 2/6/18										
*	Engineer to mark concrete repairs	1d	Wed 2/7/Wed 2/7/1										
*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu Wed 2/8/18 3/21/18										
*	Paint exterior of building	5d	Thu 3/22,Wed 3/28/										
*	Clean up/move swingstage	2d	Thu 3/29,Fri 3/30/18										
*	Line 20	40d	Mon 2/5/Fri 3/30/18										
*	Set up protection/rigging	2d	Mon 2/5/Tue 2/6/18										
*	Engineer to mark concrete repairs	1d	Wed 2/7/Wed 2/7/1										
*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d	Thu Wed 2/8/18 3/21/18										
*	Paint exterior of building	5d	Thu 3/22/Wed 3/28/										
*	Clean up/move swingstage	2d	Thu 3/29/Fri 3/30/18										
*	Line 21	40d	Mon 2/5/Fri 3/30/18										
*	Set up protection/rigging	2d	Mon 2/5/Tue 2/6/18										
*	Engineer to mark concrete repairs	1d	Wed 2/7/Wed 2/7/1										

Page 5

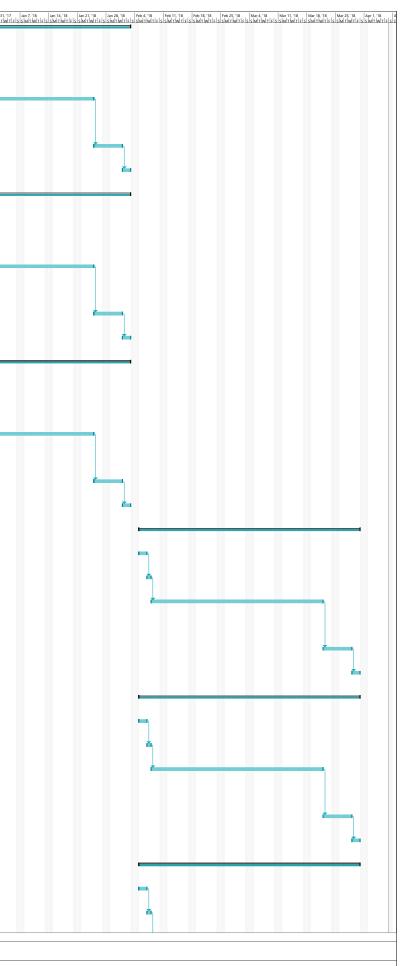

0	Task Mode	Task Name	Duration Start	Finish	
	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d Thu 2/8/	Wed 18 3/21/18	
,	*	Paint exterior of building	5d Thu	3/22,Wed 3/28	8/
1	*	Clean up/move swingstage	2d Thu	3/29/Fri 3/30/1	18
	*	Line 22	40d Mon	2/5/Fri 3/30/1	18
	*	Set up protection/rigging	2d Mon	2/5/Tue 2/6/1	18
11	*	Engineer to mark concrete repairs	1d Wed	2/7/Wed 2/7/	/1
32	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d Thu 2/8/	Wed 18 3/21/18	
33	*	Paint exterior of building	5d Thu	3/22/Wed 3/28	8/
34	*	Clean up/move swingstage	2d Thu	3/29/Fri 3/30/1	18
85	*	Line 23	40d Mon	2/5/Fri 3/30/1	18
36	*	Set up protection/rigging	2d Mon	2/5/Tue 2/6/1	18
37	*	Engineer to mark concrete repairs	1d Wed	2/7/Wed 2/7/	/1
В	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d Thu 2/8/	Wed 18 3/21/18	
19	*	Paint exterior of building	5d Thu	3/22/Wed 3/28	8/
0	*	Clean up/move swingstage	2d Thu	3/29/Fri 3/30/1	18
91	*	Line 24	40d Mon	2/5/Fri 3/30/1	18
92	*	Set up protection/rigging	2d Mon	2/5/Tue 2/6/1	18
3	*	Engineer to mark concrete repairs	1d Wed	2/7/Wed 2/7/	/1
4	*	Removal of stucco finish, repair concrete per Engineer's specifications, reapply stucco	30d Thu 2/8/	Wed 18 3/21/18	
95	*	Paint exterior of building	5d Thu	3/22/Wed 3/28	8/
96	*	Clean up/move swingstage	2d Thu	3/29/Fri 3/30/1	16
7	*	Clean Up/Punch Out	4d Mon	4/2/Thu 4/5/1	18
88	*	Demobilization	0d Fri 4	/6/18Fri 4/6/18	8

